




Tracking Finals Progress of ARRA Contracts

4/1/2012




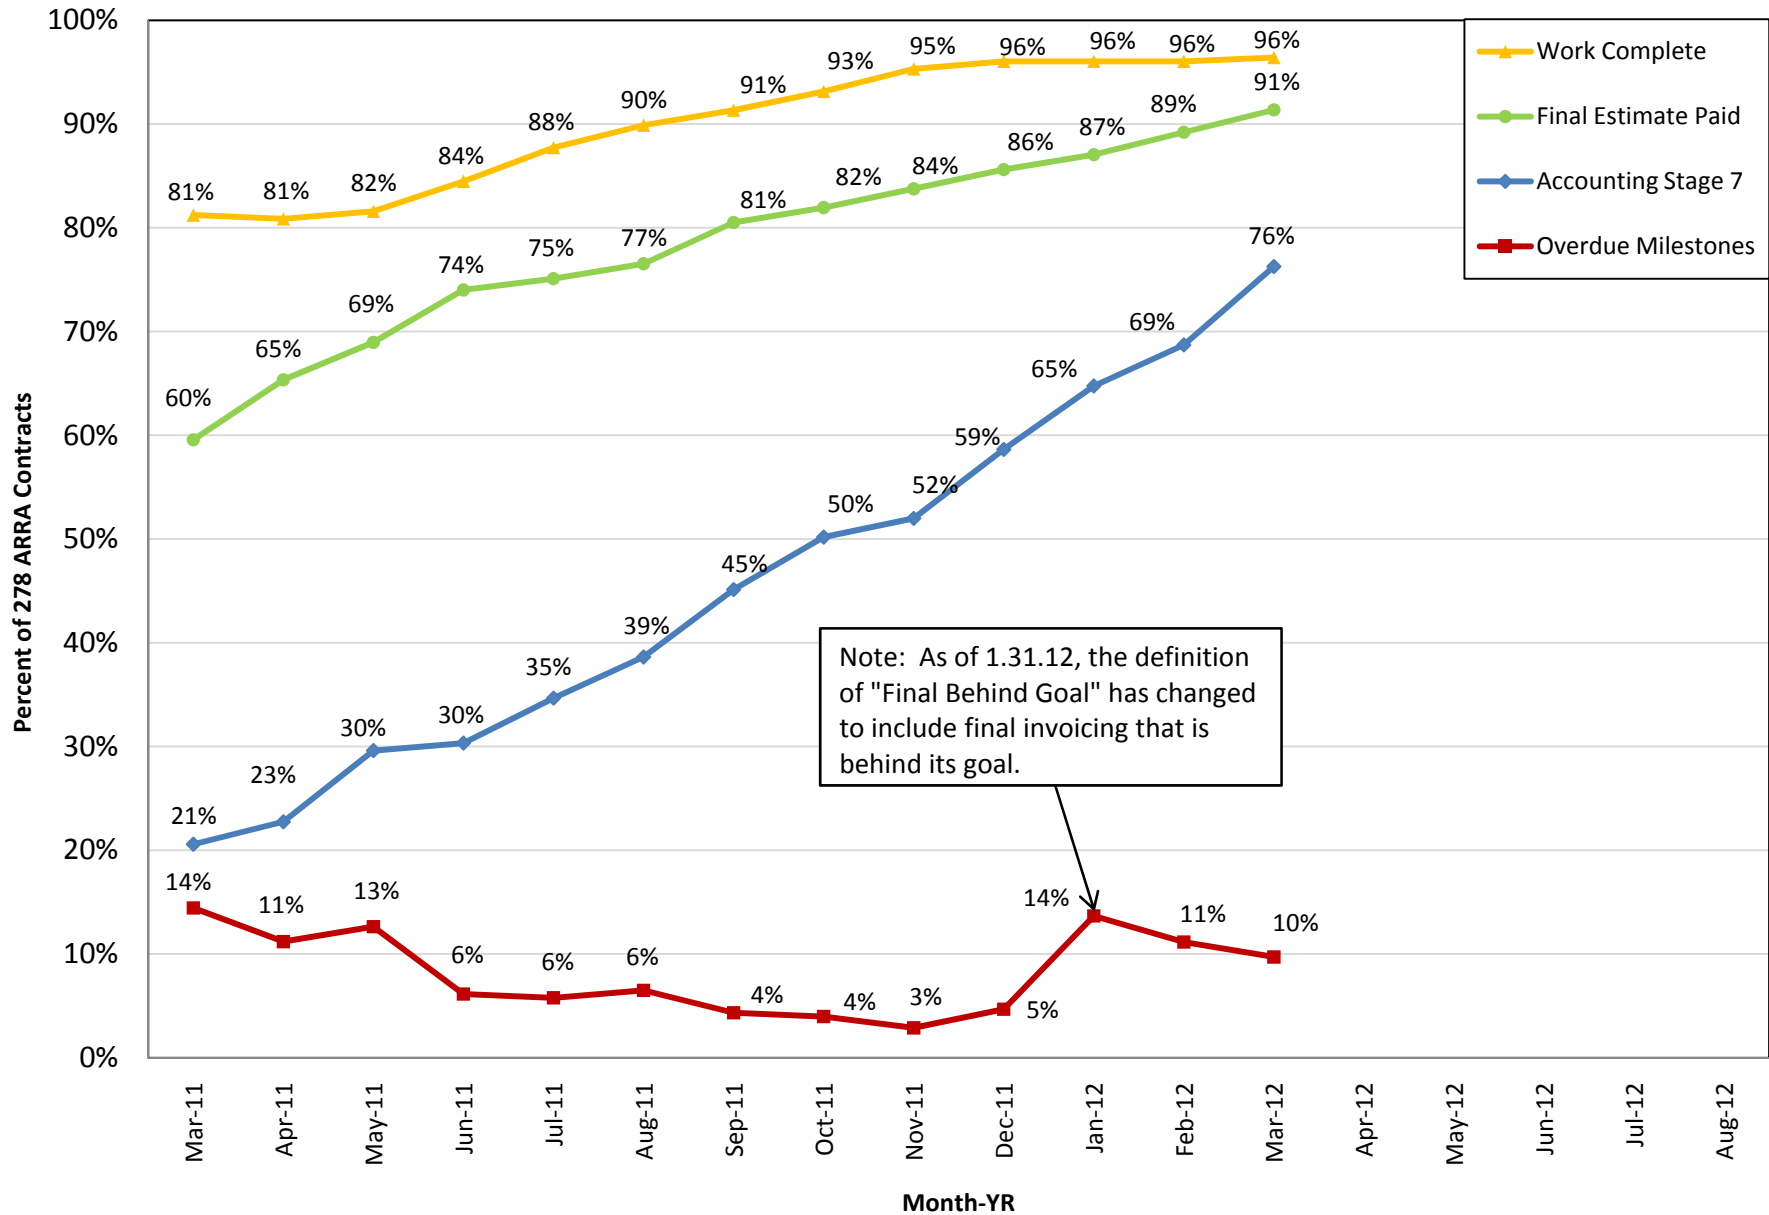

Progress of ARRA Contracts

Updated: 4/9/12

□ Number of ARRA Contracts ■ Final Estimate Paid ■ Accounting Stage 7 ■ Final Behind Goal

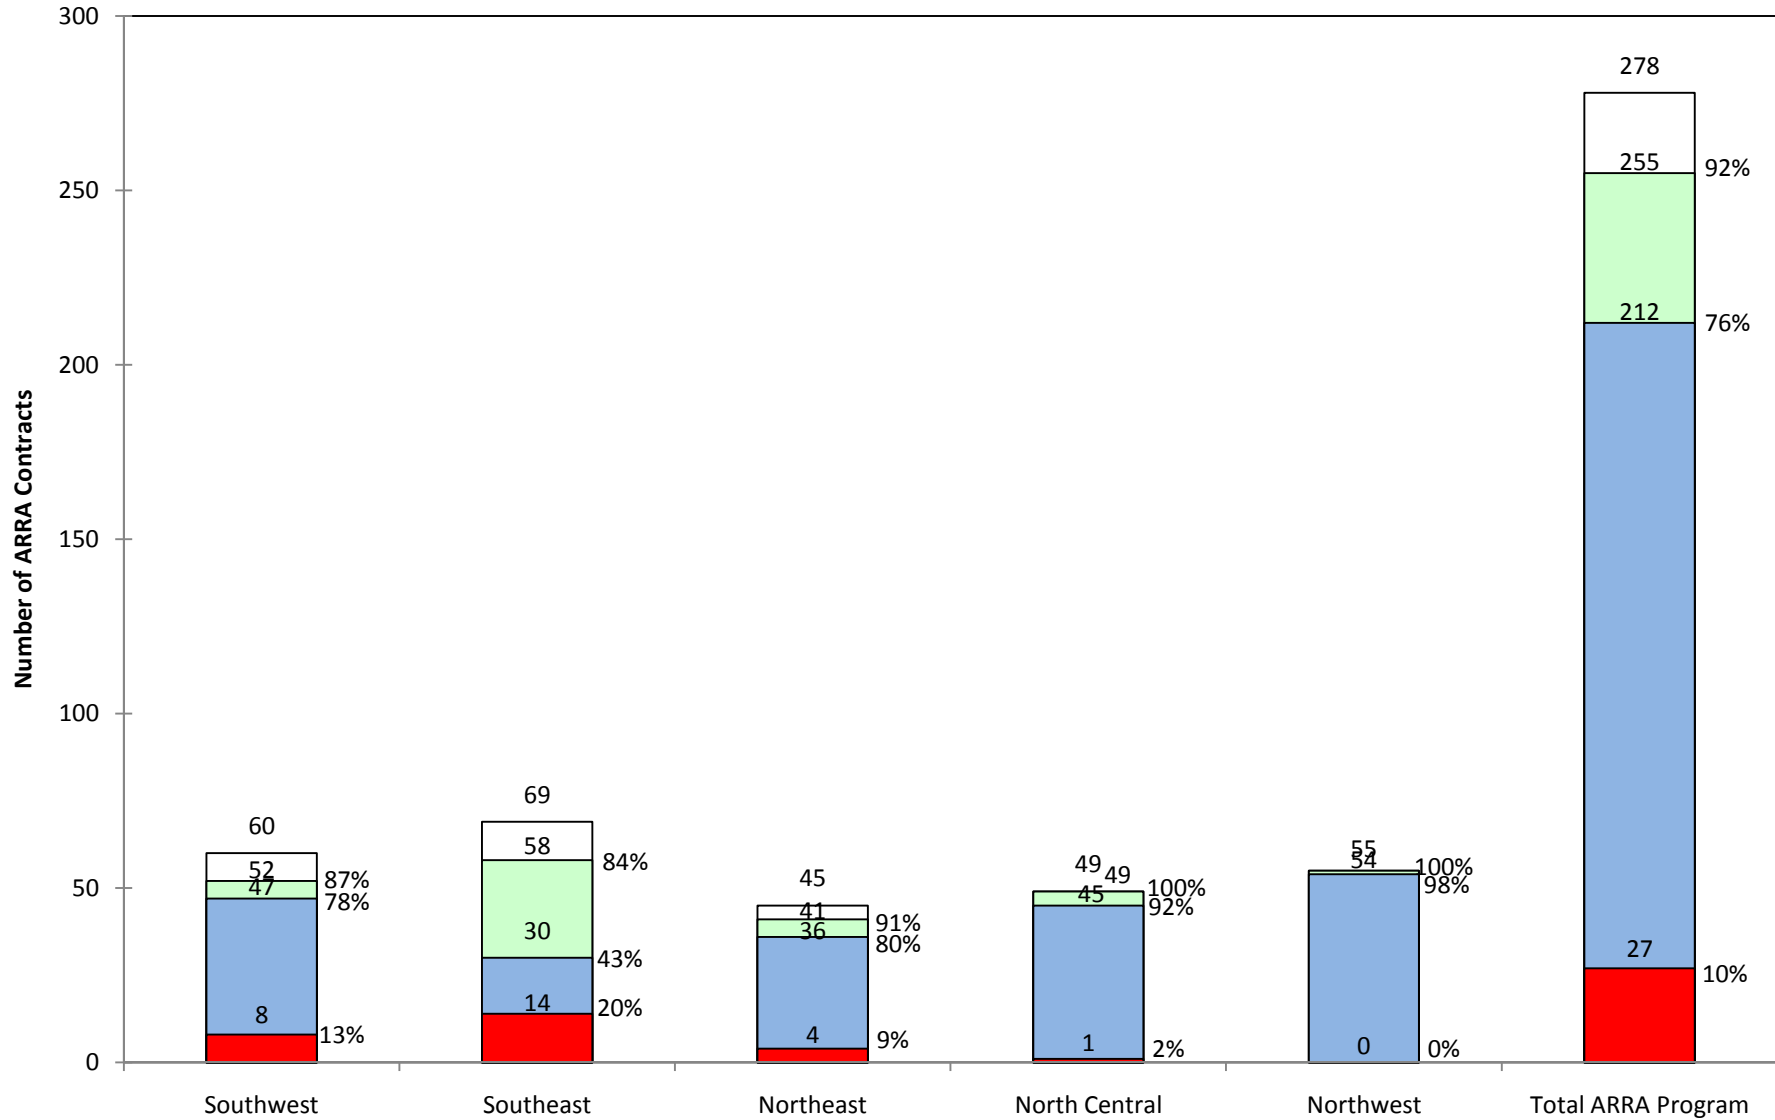



ARRA Carryover Projects

NC Region - None

NE Region - 3 Projects

State/ Local, Year	Project ID	County	Route	Carryover Type	Approximate Carryover Amt.	Anticipated Start Date	Anticipated End Date	Brief Description of remaining work
Local, 2010	6507-01-71	Outagamie	Greenville Ped Trail	Proving Period	\$0	N/A	7/30/2012	2-year Plant Cycle
Local, 2010	4566-01-71	Brown	CTH I	Unplanned	\$85,000	4/1/2012	6/30/2012	Grading & Beam Guard
Local, 2010	9281-08-71	Brown	CTH EB	Unplanned	\$65,000	4/1/2012	6/30/2012	Sidewalk Replacement

NW Region - None

SE Region - 4 Projects

State/ Local, Year	Project ID	County	Route	Carryover Type	Approximate Carryover Amt.	Anticipated Start Date	Anticipated End Date	Brief Description of remaining work
Local, 2010	2990-02-70	Milwaukee	Streetscaping	Proving Period	\$0	N/A	10/15/2012	2-year plant cycle
Local, 2010	3735-01-70	Kenosha	Streetscaping	Proving Period	\$0	N/A	10/15/2012	2-year plant cycle
Local, 2010	2984-07-70	Milwaukee	Hank Aaron State Trl	Proving Period	\$0	N/A	10/15/2012	2-year plant cycle
Local, 2010	3846-00-71	Walworth	Wrigley Dr.	Unplanned	\$0	4/1/2012	5/1/2012	Hand rail paint touchup. Ongoing issues with platform not meeting building code specs.

SW Region - 2 Projects

State/ Local, Year	Project ID	County	Route	Carryover Type	Approximate Carryover Amt.	Anticipated Start Date	Anticipated End Date	Brief Description of remaining work
State, 2009	1066-02-72	Dane	I-94	Unplanned	\$126,000	5/1/2012	6/30/2012	Emulsified Asphalt Median Treatment, Crushed Aggregate Slope Paving at Gaston and Milwaukee
Local, 2010	5984-00-73	Grant	Cassville Car Ferry	Unplanned	\$0	Present	7/31/2012	Ongoing issues with the steering. The boat is out of the water and back at the Contractor's. They are currently working on fixing it. Warranty expires 7/2012



ARRA Project with Proving Periods

NC Region - None

NE Region - 2 Projects				Paint Proving Periods				Plant Establishment Periods			
State/ Local, Year	Project ID	County	Route	Y/N	Pvt Mrking Finished	Proving Period (days)	Proving Period Expires	Y/N	Initial Completion of Planting	Est. Period (yrs)	Est. Period Ends
Local, 2010	4996-01-69	Sheboygan	Taylor Dr.	Y	10/31/2011	180	4/28/2012	Y	10/22/2010	1	10/31/2011
Local, 2010	6507-01-71	Outagamie	Greenville Ped Trail	Y	9/30/2010	197	4/15/2011	Y	9/21/2010	2	7/30/2012

NW Region - None

SE Region - 7 Projects				Paint Proving Periods				Plant Establishment Periods			
State/ Local, Year	Project ID	County	Route	Y/N	Pvt Mrking Finished	Proving Period (days)	Proving Period Expires	Y/N	Initial Completion of Planting	Est. Period (yrs)	Est. Period Ends
Local, 2010	2355-00-76	Milwaukee	CTH ZZ	Y	7/31/2011	259	4/15/2012	N			
Local, 2010	2704-07-70	Kenosha	14th St	Y	8/31/2011	228	4/15/2012	N			
Local, 2010	2656-00-71	Milwaukee	70th St	Y	6/30/2011	290	4/15/2012	N			
Local, 2010	2020-01-70	Milwaukee	S. 51st St.	Y	10/8/2010	189	4/15/2011	Y	10/13/2010	2	10/15/2012
Local, 2010	2984-07-70	Milwaukee	Hank Aaron State Trl	N				Y	12/5/2010	2	10/15/2012
Local, 2010	2990-02-70	Milwaukee	Streetscaping	Y	10/31/2010	180	4/29/2011	Y	10/29/2010	2	10/15/2012
Local, 2010	3735-01-70	Kenosha	Streetscaping	Y	10/31/2010	180	4/29/2011	Y	10/18/2010	2	10/15/2012

SW Region - None
